


SP 4006-35 TH 60 Project Update for the Public

Anticipated Work for the week April 19th – April 26th


- Centerline and approach culvert removal and replacement from 222nd St. on TH 60 to 7th St. in the City of Madison Lake.
- Centerline and approach culvert work from 251st Ave. to CSAH 13 on TH 60.
- Various driveway culverts will be worked on throughout the project.
*There will be short-term delays.
- Excavation and embankment work at 222nd St.
- Excavation and embankment work at CSAH 44.
- The City of Madison Lake work will generally be limited to 7th St. to 5th St.
*The residents of Madison Lake should be aware that construction traffic and activities will be present along all locations in the vicinity of Walnut Ave.
- Resident and Business access will be limited from 7th St. to 3rd St.
- The work associated with the City of Madison Lake will be conducted in 2 separate phases. Phase 1 will be from 7th St. to the area of 3rd St. Once Phase 1 is completed, Phase 2 will begin and take off from the area of 3rd St. to approximately 500 east of 1st.

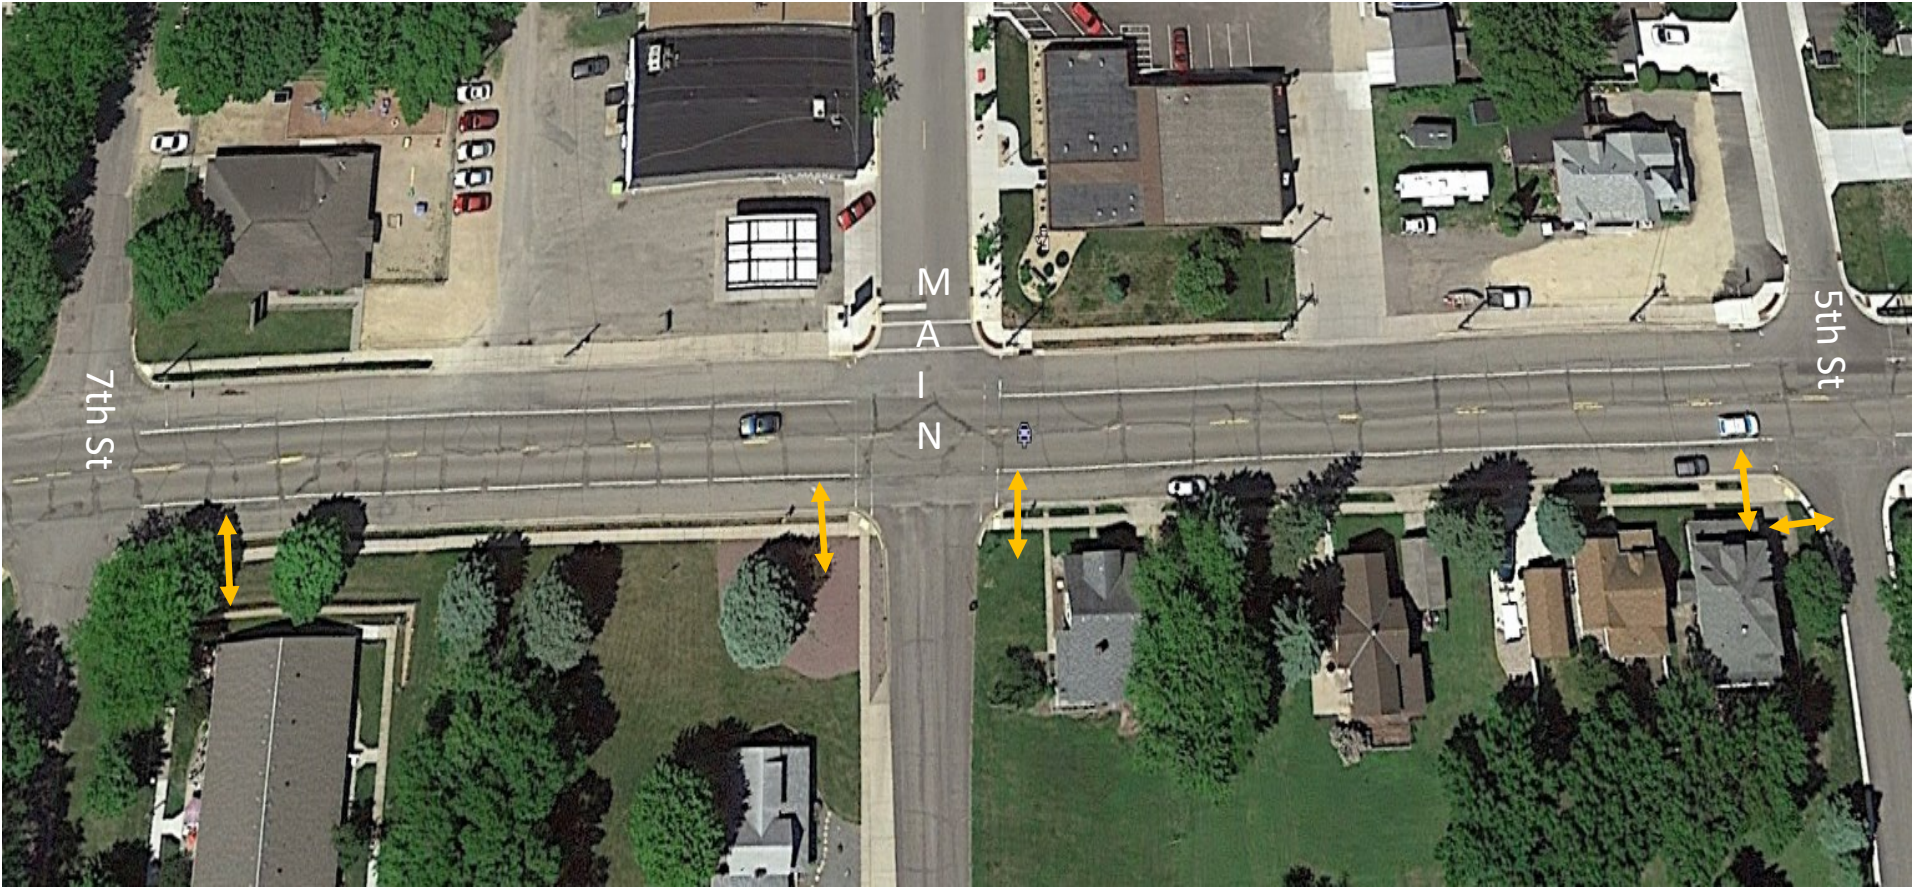

Sidewalk Closed Sign

Road Crossing - Available most of the time

Pedestrian Crossing

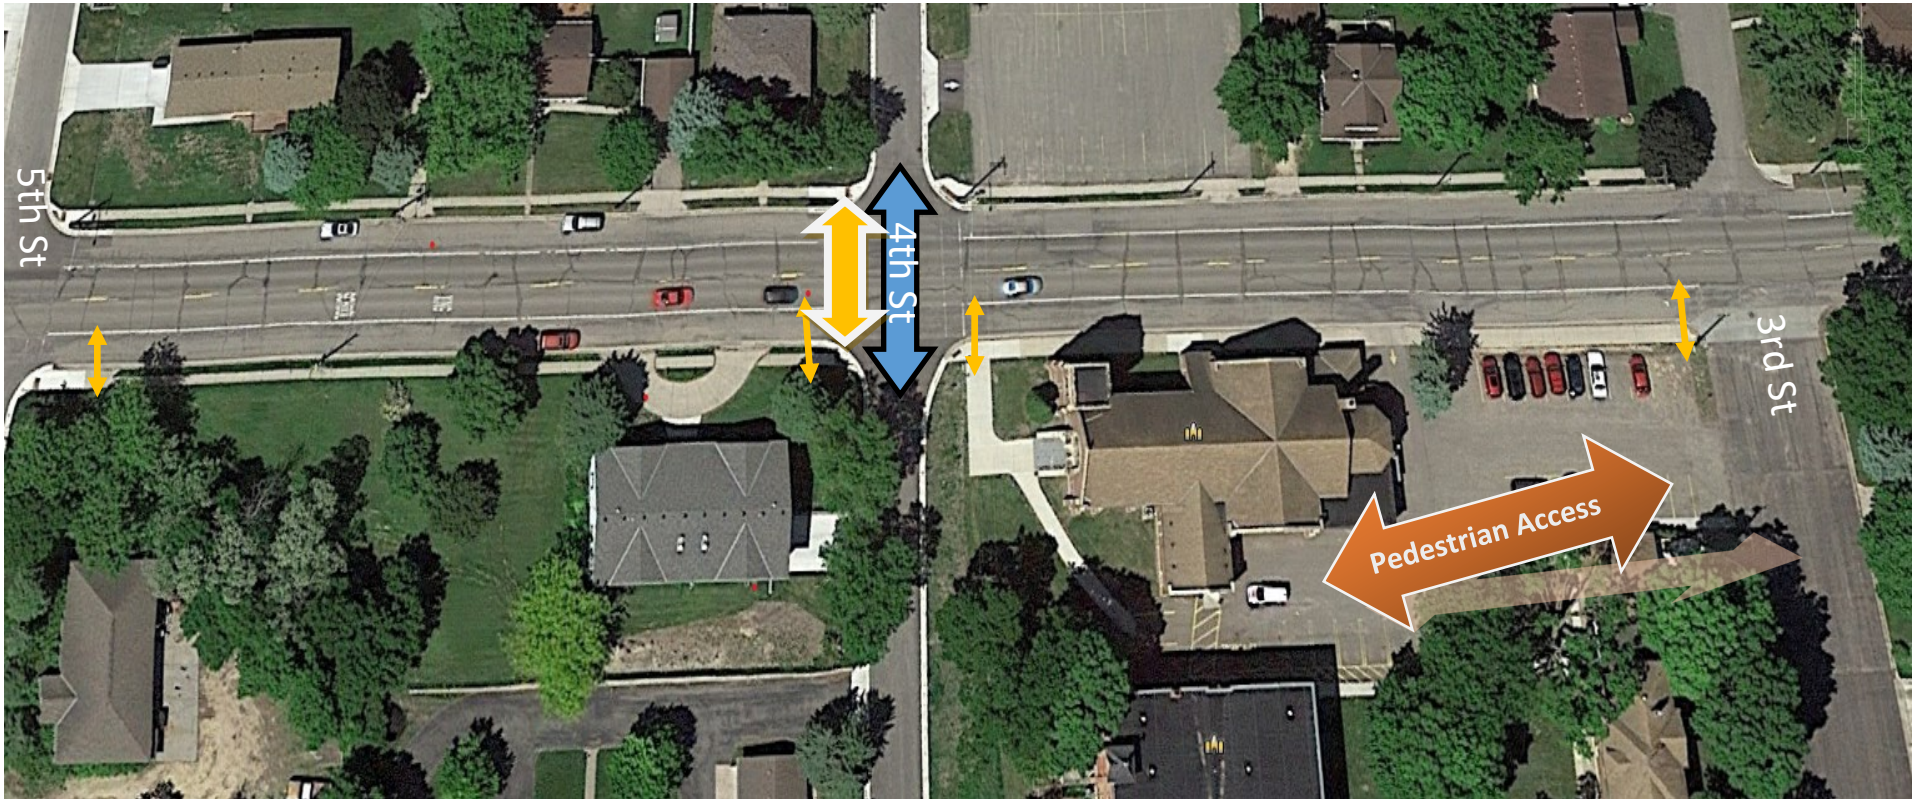

Sidewalk Closed Sign



Road Crossing - Available most of the time



Pedestrian Crossing
